

Feb 17, 2021 - 3:14pm F:\Project\190 - SUCF\190760004 SUNY Brockport New Campus Drive\Design\CADD\021028-02 - Reconstruct New Campus Drive & Cooper Hall\Sheet Files\190760004_G-006.dwg

COORDINATION NOTES:

1. CONTRACTOR SHALL PROVIDE KEYS TO GATE LOCKS TO THE OWNER'S SITE REPRESENTATIVE, CAMPUS POLICE, AND VILLAGE OF BROCKPORT FIRE DEPARTMENT. ANY PROPOSED REVISIONS TO THE FENCE, GATE, AND BUILDING ACCESS LAYOUT SHALL BE COORDINATED WITH THE OWNER'S REPRESENTATIVE, CAMPUS POLICE, AND THE VILLAGE OF BROCKPORT FIRE DEPARTMENT.
2. THE CONTRACTOR WILL BE RESPONSIBLE FOR ANY LAWN MOWING AND MAINTENANCE REQUIRED WITHIN THE FENCED AREAS. GRASS SHALL NOT EXCEED A HEIGHT OF FOUR INCHES PRIOR TO MOWING.
3. THE CONTRACTOR WILL BE RESPONSIBLE FOR SNOW REMOVAL AS NEEDED WITHIN THE FENCED AREAS. CAMPUS WILL PROVIDE SNOW REMOVAL AS NECESSARY ALONG THE AREAS THAT WILL BE DESIGNATED AS ACCESSIBLE TO THE CAMPUS COMMUNITY. CONTRACTOR SHALL PROVIDE ACCESS AS NECESSARY FOR CAMPUS SNOW REMOVAL EQUIPMENT.
4. COORDINATE WORK AREA FENCING WITH TREE AND SOIL PROTECTION PLANS.
5. THE CONTRACTOR SHALL BE RESPONSIBLE FOR CONSTRUCTION SEQUENCING AND THE PROTECTION OF EXISTING AND ADJACENT STRUCTURES DURING DEMOLITION AS NECESSARY TO PREVENT UNDERMINING EXISTING FOUNDATIONS OR DAMAGING EXISTING STRUCTURES.
6. CONSTRUCTION FENCE WILL NEED TO BE RELOCATED AT AREAS WHERE SITE IMPROVEMENTS EXTEND OUTSIDE OF PROVIDED LAYOUT. CONTRACTOR TO COORDINATE WITH UTILITY AND SITE IMPROVEMENT PLANS AND MOVE FENCE AS NEEDED TO FACILITATE INSTALLATION OF NEW WORK.
7. CONTRACTOR TO DECOMPACT / SCARIFY SUBGRADE OF TEMPORARY ASPHALT WALKS PRIOR TO PLACEMENT OF TOPSOIL, SEED AND SOD.
8. CONTRACTOR TO REFER TO SHEET G-008 FOR VEHICULAR DETOUR SIGNAGE PLAN REQUIREMENTS DURING CONSTRUCTION PHASE 2021.
9. MAIN ENTRANCE WELCOME SIGN TO BE CONSTRUCTED IN PHASE 2021.

LEGEND:


- TEMPORARY CONSTRUCTION FENCE FOR CONSTRUCTION SEASON
- PEDESTRIAN WALKWAY ACCESS DURING CONSTRUCTION
- TEMPORARY SIGNAGE, REFER TO G-014 FOR KEYED SIGN NOTES
- TEMPORARY ASPHALT PAVEMENT WALKWAY (8'-0" WIDTH) (SEE NOTES ON SHEET G-014)
- HC HANDICAP ACCESSIBLE BUILDING ENTRANCE

PROJECT SCHEDULE / PHASING DEFINITION

REFER TO SPECIFICATION 013213 FOR SPECIAL PROJECT SCHEDULE AND PHASING REQUIREMENTS.

KEYED NOTES:

- CONTRACTOR ACCESS TO PROJECT FROM OFFSITE. CONTRACTOR TO UTILIZE FLAGGERS ENTERING AND EXITING CONSTRUCTION SITE AT ALL TIMES, INCLUDING DELIVERY OF EQUIPMENT AND MATERIALS. REFER TO SPECIFICATION SECTION 340133. DRUM BARRICADES TO BE IN PLACE AT ALL TIMES DURING CONSTRUCTION INDICATING ROAD CLOSURE. CONTRACTOR TO VERIFY BARRICADES ARE IN PLACE AT THE END OF EACH CONSTRUCTION DAY. FIRE DEPARTMENT AND EMERGENCY ACCESS FROM THIS POINT TO BE MAINTAINED AT ALL TIMES DURING CONSTRUCTION.
- PEDESTRIAN ACCESS ACROSS NEW CAMPUS DURING CONSTRUCTION VIA OVERHEAD WALKWAY ACCESSED FROM DRAKE MEMORIAL LIBRARY AND TUTTLE NORTH. CONTRACTOR TO INSTALL BUILDING INTERIOR DETOUR SIGNAGE.
- UTILITY INSTALLATION AND SITE RESTORATION WORK TO OCCUR OUTSIDE OF LIMITS OF TEMPORARY CONSTRUCTION FENCE. CONTRACTOR TO PROVIDE NECESSARY FLAGGERS AND LANE SHUTDOWNS AT REQUIRED FOR INSTALLATION. COORDINATE ANY SIDEWALK SHUTDOWNS WITH CAMPUS AND OWNER'S REPRESENTATIVE.
- WATER UTILITY WORK INSTALLATION TO OCCUR OUTSIDE OF LIMITS OF TEMPORARY CONSTRUCTION FENCE. CONTRACTOR TO LIMIT SHUTDOWN OF COMMENCEMENT DRIVE AND NEW CAMPUS DRIVE TO A SINGLE LANE AT A TIME DURING WORK AND PROVIDE MAINTENANCE AND PROTECTION OF TRAFFIC PER DETAIL B1/C-504.

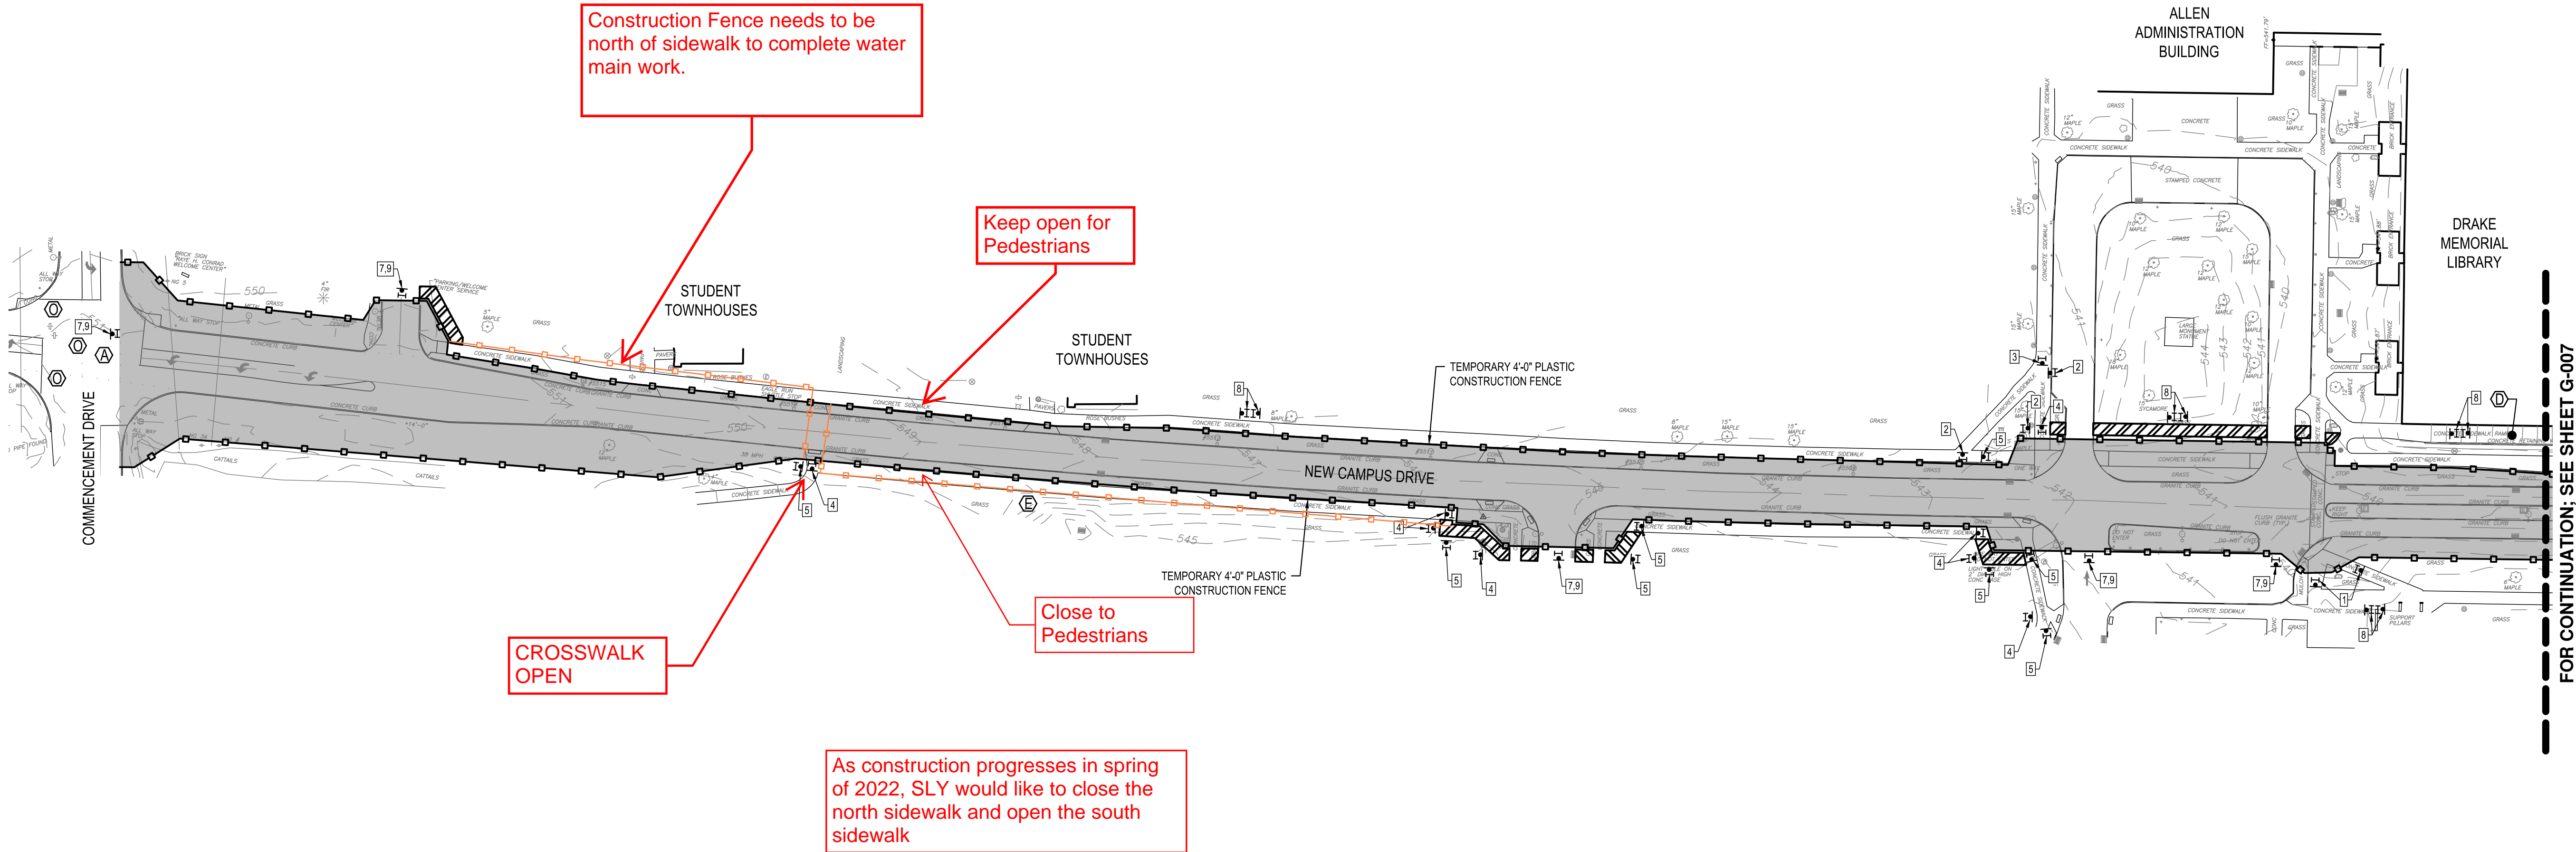

A1 PHASING PLAN

SCALE: 1" = 60'

0 60' 120'

STATE UNIVERSITY CONSTRUCTION
FUND PROJECT #021028-02
RECONSTRUCT NEW CAMPUS DRIVE
& COOPER HALL DROP OFF
THE COLLEGE AT BROCKPORT

MARK	DATE	DESCRIPTION
REVISIONS		
PROJECT NO:	190.760.004	
DATE:	FEBRUARY 17, 2021	
DRAWN BY:	K.C.MAGILL-JONES	
DESIGNED BY:	K.C.MAGILL-JONES	
CHECKED BY:	D.H.WETHEY, P.E.	
NO ALTERATION PERMITTED HEREON EXCEPT AS PROVIDED UNDER SECTION 7209 SUBDIVISION 2 OF THE NEW YORK EDUCATION LAW		

GENERAL

PHASING
PLAN
2021

G-006
